

## INFORMATION REPORT

REPORT

CD NO.

COUNTRY East Germany

DATE DISTR. 11 December 1957

SUBJECT Construction Work at Stendal Airfield

NO. OF PAGES 4

PLACE ACQUIRED [REDACTED]

50X1-HUM

DATE OF INFO

NO. OF PAGES

SUPPLEMENT TO  
REF ID: 50X1-HUM

PROCESSING COPY

This document contains neither recommendations nor conclusions of the Defense Intelligence Agency. It has been reviewed and approved for release under the Freedom of Information Act. Its transmission or the regulation of its contents by law other than an unauthorized person is prohibited. Re-use or re-distribution of this form is prohibited.

1. The concrete cover of the two ends of the runway each 520 meters long was 20 cm thick, while the cover of the middle portion was only 18 cm thick. Runway and taxiway had the same profiles. From a vertex in the first third toward the eastern end of the two lanes, they inclined toward west by about 14.5 meters and toward east by about 2.45 meters. Portland cement type 325 with a compressive strength of 325 kg/cm<sup>2</sup> was used. The following layers were underneath the concrete cover (from top to bottom):

Insulating cardboard

10 cm sand

20 cm gravel (packed)

Subsoil

ENCLOSURE ATTACHED

PLEASE ROUTE

Concreting work on all concrete lanes and hard stands were scheduled to be completed by 10 October 1957. The 1-meter-wide and 40-cm-thick border strip was reinforced by 10-cm layers of macadam and 10-cm layers of topsoil alternating with one another.<sup>2</sup> Joints were filled with bitumen. Border strip and joints of all concrete lanes and slabs were to be completed by 31 October 1957.

2. Cable collecting shafts were installed underneath the runway, taxiway, auxiliary collecting lanes.

Thirty-six collecting shafts each were installed on the two sides of the runway, with decreasing intervals toward the two ends of the runway from the vertex. They were connected by pipes manufactured with concrete moulded by centrifugal action. Pipes increasing not only in number, but also in diameter toward the ends of the runway from 250 mm at the vertex to 700 mm were installed to secure a constant discharge of water which otherwise would easily dam up at the sloping ends.<sup>2</sup> The northern-most collectors of the eastern and western ends of the runway were connected with the corresponding southern-most collectors. From the two southern collecting shafts, water was conducted through a pipe 700 mm in diameter to the western and to the eastern outflow respectively.<sup>1</sup> Rain water ran from a gutter extending along the two sides of the runway through so-called rain collectors and concrete pipes 200 mm in diameter to the collecting shafts or their connecting pipes.<sup>2</sup> A total of 14 rain collectors was installed at each side of the runway. The drainage of the auxiliary lane was also secured by the installation of collecting shafts.

50X1-HUM

CLASSIFICATION SECRET//NOFORN

DATE	TYPE	FILE #	DISPOSITION				
12/11/57	PK	100					

50X1-HUM

SECRET  
NOFORN

50X1-HUM


- 2 -

3. The following safety strips and zones consisting of a layer of mineral soil 20 cm thick were available:  
A 220-meter wide strip along the southern side of the runway.  
A 70-meter wide strip along the northern side of the auxiliary lane.  
A 60-meter wide strip running on each side of the northern approach taxiway.  
A 60-meter wide strip from the western end of the auxiliary lane to the spur track along the western approach taxiway.  
A 70-meter wide strip along the northern side of this approach lane.  
Further safety strips were built between runway and taxiway and between taxiway and auxiliary lane.
4. Repair work on the 3 western hangars, each 36 x 100 meters, at the northeastern portion of the airfield was scheduled to be completed by late September 1957, and on the two eastern hangars after the departure of the ITB (Ing. Tiefbau Brandenburg) construction personnel.
5. The fuel dumps installed prior to 1945 will possibly be put into operation, since no new fuel dumps were observed. The old dumps were empty and their capacity was unknown.  
[redacted] the 3 fuel dumps had formerly been interconnected.  
Fuel dump No 1 contained four tanks, dump No 2 three tanks, and dump No 3 six tanks. A manhole led to the underground bedding of each tank. The concrete cover of fuel dump No 3 was about 3 meters high and the tank below the concrete cover was about 8 meters high.
6. The installation of a hydraulic station with 2 air-pressure tanks 1.60 meters in diameter, 2 pressure pumps, and 2 15 kW reserve pumps was planned.

Description of Attachment:

A sketch showing installations described in the legend.

50X1-HUM



SECRET  
NOFORN

SECRET -

NOFORN

Annex 1

50X1-HUM

-- 2 --

Legend

Overlay sketch, scale 1:12,500  
Sheet 3336/37

Stendal Airfield,

50X1-HUM

- I Runway 2,000 x 60 meters
- R Taxiway 14 meters wide
- II Connecting lanes 14 meters wide
- III " " " "
- IV " " " "
- V " " 12 " "
- VI " " 12 " "
- VII Auxiliary lane 692 x 50 meters
- VIII Northern approach taxiway 12 meters wide
- IX Connecting lane between runway and taxiway 14 meters wide, between taxiway and auxiliary lane 12 meters wide
- X Western dispersal area 160 x 30 meters
- XI Eastern dispersal area 80 x 30 meters
  
- 1 Fuel dump No 1 : 4 tanks
- 2 Fuel dump No 2 : 3 tanks
- 3 Fuel dump No 3 : 6 tanks
- 4 Spur track - ramp
- 5 Western approach taxiway 10 meters wide
- 6 Ordnance depot
- 7 Fence
- 8 Entrance
- 9 Eastern water discharge point
- 10 Western water discharge point
- 11 Cable collecting shafts underneath the runway and taxiway
- 12 Drainage system
- 13 Safety zone

SECRET -


NOFORN

SECRET  
NOFORN

Lanez 2

50X1-HUM

Vertical Section of the runway

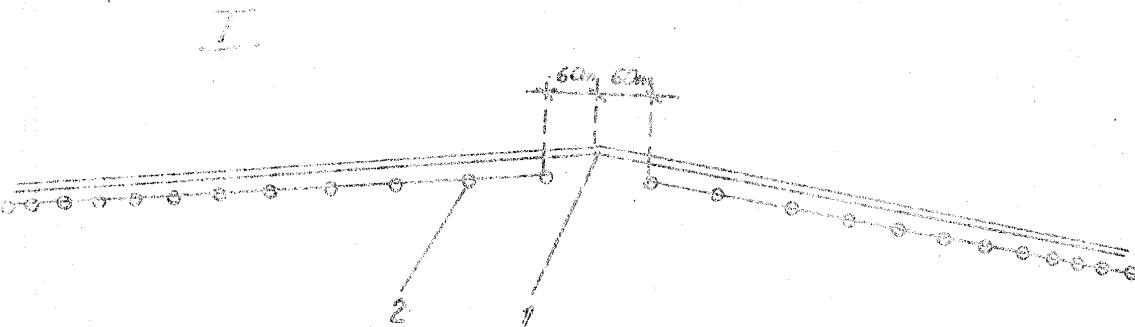


Legend

1. Vertex of the runway
2. Cable collecting shafts

11

Cross Section of the runway

Not to Scale

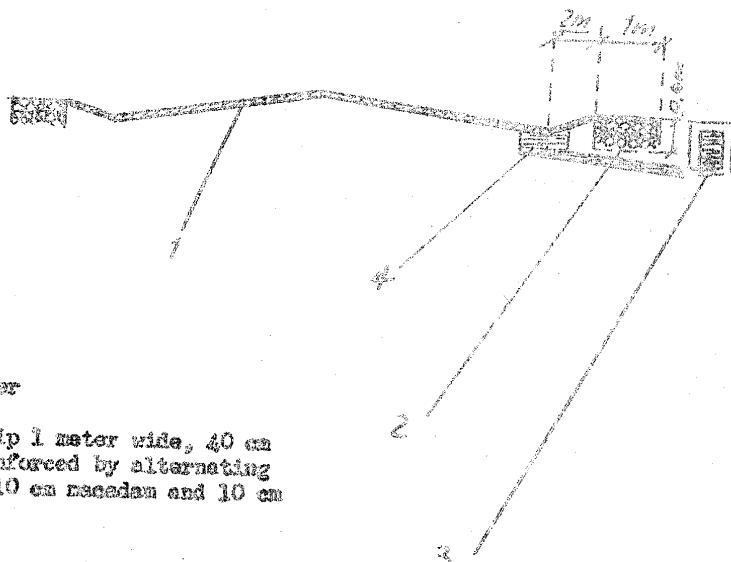

Legend

1. Runway cover
2. Border strip 1 meter wide, 40 cm thick, reinforced by alternating layers of 10 cm macadam and 10 cm topsoil
3. Collector
4. Main collector with pipes 200 mm in diameter

SECRET  
NOFORN

**SECRET  
U.S. OFFICIALS ONLY  
CLASSIFICATION**

COUNTRY East Germany

SUBJECT Construction Work at Stendal Airfield

DATE OF REPORT 13 November 1957

REPORT

PLACE ACQUIRED

50X1-HUM

LAST REPORT ON SUBJECT  
(If applicable)ANNEXES 2-sketches with  
legends on ditto

1. The concrete cover of the two ends of the runway each 520 meters long was 20 cm thick, while the cover of the middle portion was only 18 cm thick. Runway and taxiway had the same profiles. From a vertex in the first third toward the eastern end of the two lanes, they inclined toward west by about 14.5 meters and toward east by about 2.45 meters. Portland cement type 325 with a compressive strength of 325 kg/cm<sup>2</sup> was used. The following layers were underneath the concrete cover (from top to bottom):

Insulating cardboard

10 cm sand

20 cm gravel (packed)

Subsoil

Concreting work on all concrete lanes and hard stands were scheduled to be completed by 10 October 1957. The 1-meter-wide and 40-cm-thick border strip was reinforced by 10-cm layers of macadam and 10-cm layers of topsoil alternating with one another.<sup>2</sup> Joints were filled with bitumen. Border strip and joints of all concrete lanes and slabs were to be completed by 31 October 1957.

2. Cable collecting shafts were installed underneath the runway, taxiway, auxiliary collecting lanes.

Thirty-six collecting shafts each were installed on the two sides of the runway, with decreasing intervals toward the two ends of the runway from the vertex. They were connected by pipes manufactured with concrete moulded by centrifugal action. Pipes increasing not only in number, but also in diameter toward the ends of the runway from 250 mm at the vertex to 700 mm were installed to secure a constant discharge of water which otherwise would easily dump up at the sloping ends.<sup>2</sup> The northern-most collectors of the eastern and western ends of the runway were connected with the corresponding southern-most collectors. From the two southern collecting shafts, water was conducted through a pipe 700 mm in diameter to the western and to the eastern outflow respectively.<sup>1</sup> Rain water ran from a gutter extending along the two sides of the runway through so-called rain collectors and concrete pipes 200 mm in diameter to the collecting shafts or their connecting pipes.<sup>2</sup> A total of 14 rain collectors was installed at each side of the runway. The drainage of the auxiliary lane was also secured by the installation of collecting shafts.

50X1-HUM

50X1-HUM

SECRET - U.S. OFFICIALS ONLY

50X1-HUM

- 2 -

3. The following safety strips and zones consisting of a layer of mineral soil 20 cm thick were available:  
A 220-meter wide strip along the southern side of the runway.  
A 70-meter wide strip along the northern side of the auxiliary lane.  
A 60-meter wide strip running on each side of the northern approach taxiway.  
A 60-meter wide strip from the western end of the auxiliary lane to the spur track along the western approach taxiway.  
A 70-meter wide strip along the northern side of this approach lane.  
Further safety strips were built between runway and taxiway and between taxiway and auxiliary lane.
4. Repair work on the 3 western hangars, each 36 x 100 meters, at the northeastern portion of the airfield was scheduled to be completed by late September 1957, and on the two eastern hangars after the departure of the ITB (Ing. Tiefbau Brandenburg) construction personnel.
5. The fuel dumps installed prior to 1945 will possibly be put into operation, since no new fuel dumps were observed. The old dumps were empty and their capacity was unknown.  
[redacted] the 3 fuel dumps had formerly been interconnected.  
Fuel dump No 1 contained four tanks, dump No 2 three tanks, and dump No 3 six tanks. A manhole led to the underground bedding of each tank. The concrete cover of fuel dump No 3 was about 3 meters high and the tank below the concrete cover was about 8 meters high.
6. The installation of a hydraulic station with 2 air-pressure tanks 1.60 meters in diameter, 2 pressure pumps, and 2 15 kW reserve pumps was planned.

1. [redacted] Comment. For sketch, see Annex 1.

50X1-HUM

2. [redacted] Comment. For sketch, see Annex 2.

50X1-HUM

SECRET - U.S. OFFICIALS ONLY

SECRET - U.S. OFFICIALS ONLY

Annex 1

50X1-HUM

- 2 -

Legend

Overlay sketch, scale 1:12,500  
Sheet 3336/57

Stendal Airfield,

50X1-HUM

- I Runway 2,000 x 60 meters
- R Taxiway 14 meters wide
- II Connecting lanes 14 meters wide
- III " " " "
- IV " " " "
- V " " 12 " "
- VI " " 12 " "
- VII Auxiliary lane 692 x 50 meters
- VIII Northern approach taxiway 12 meters wide
- IX Connecting lane between runway and taxiway 14 meters wide, between taxiway and auxiliary lane 12 meters wide
- X Western dispersal area 160 x 30 meters
- XI Eastern dispersal area 80 x 30 meters
  
- 1 Fuel dump No 1 : 4 tanks
- 2 Fuel dump No 2 : 3 tanks
- 3 Fuel dump No 3 : 6 tanks
- 4 Spur track - ramp
- 5 Western approach taxiway 10 meters wide
- 6 Ordnance depot
- 7 Fence
- 8 Entrance
- 9 Eastern water discharge point
- 10 Western water discharge point
- 11 Cable collecting shafts underneath the runway and taxiway
- 12 Drainage system
- 13 Safety zone


SECRET - U.S. OFFICIALS ONLY

SECRET - U.S. OFFICIALS ONLY

Annex 2

50X1-HUM

Longitudinal Section of the Runway

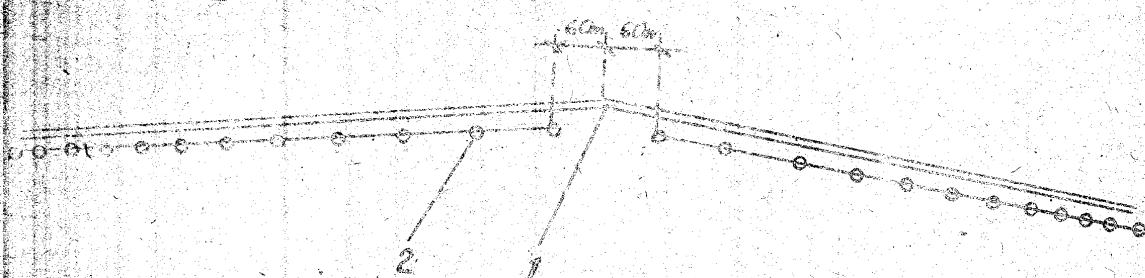


Legend

1. Vertex of the runway
2. Cable collecting shafts

Cross Section of the runway

'Not to Scale'

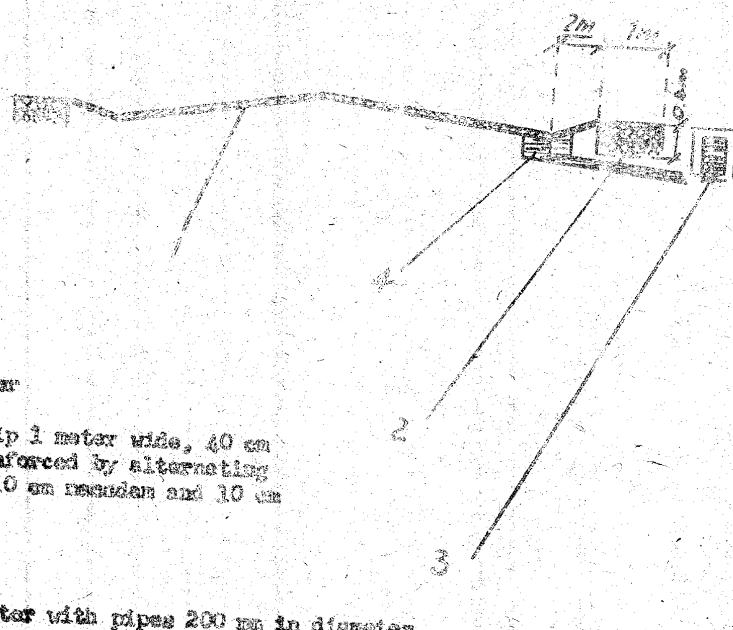

Legend

1. Runway cover
2. Border strip 1 meter wide, 40 cm thick, reinforced by alternating layers of 10 cm macadam and 10 cm topsoil
3. Collector
4. Rain collector with pipes 200 mm in diameter

SECRET - U.S. OFFICIALS ONLY

**SECRET**  
**US OFFICIALS ONLY**

